ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
1			**Software**	**37 days**	**Fri 1/10/14**	**Mon 3/3/14**	
2			Data Analysis	26 days	Fri 1/10/14	Fri 2/14/14	
3			Upgrades	12 days	Fri 2/14/14	Mon 3/3/14	
4			**Shore Side**	**81 days**	**Wed 1/8/14**	**Wed 4/30/14**	
5			Matlab review scripts	36 days	Mon 3/10/14	Mon 4/28/14	
6			Poster Prep	23 days	Wed 1/8/14	Fri 2/7/14	
7			Poster Presentation ASLO	0 days	Thu 2/27/14	Thu 2/27/14	
8			Animation STOQs Integration	11 days	Mon 3/10/14	Mon 3/24/14	
9			**Wave Glider**	**68 days**	**Mon 1/27/14**	**Wed 4/30/14**	
10			Fair xducer	28 days	Mon 3/24/14	Wed 4/30/14	
11			SV3 Integration	21 days	Mon 1/27/14	Mon 2/24/14	
12			**Electrical**	**16 days?**	**Mon 1/13/14**	**Tue 2/4/14**	
13			BED #2 prep				
14			Order Batteries	0 days	Tue 2/4/14	Tue 2/4/14	
15			Fix WG electrical wiring	16 days	Mon 1/13/14	Mon 2/3/14	
16			**Mechanical**	**55 days**	**Mon 1/13/14**	**Fri 3/28/14**	
17			Pressure sensor upgrade	31 days	Mon 1/13/14	Mon 2/24/14	
18			Pressure sensor cal	24 days	Tue 2/25/14	Fri 3/28/14	17
19			Integrate acoustic pole	0 days	Thu 1/16/14	Thu 1/16/14	
20			**Systems**	**215 days?**	**Mon 1/13/14**	**Mon 11/10/14**	
21			Calibrate USBL	4 days	Thu 1/16/14	Tue 1/21/14	
22			RTC calibration	35 days	Mon 1/13/14	Fri 2/28/14	
23			Carson cruise	0 days	Tue 3/4/14	Tue 3/4/14	
24			Carson cruise	0 days	Mon 11/10/14	Mon 11/10/14	
25			CDR	0 days	Tue 2/11/14	Tue 2/11/14	
26			Construct 7 BEDs				
27			**Operations**	**343 days**	**Thu 7/18/13**	**Mon 11/10/14**	
28			BED #2 Deployment	106 days	Thu 7/18/13	Thu 12/12/13	
29			BED/Monument Deployment	238 days	Thu 12/12/13	Mon 11/10/14	

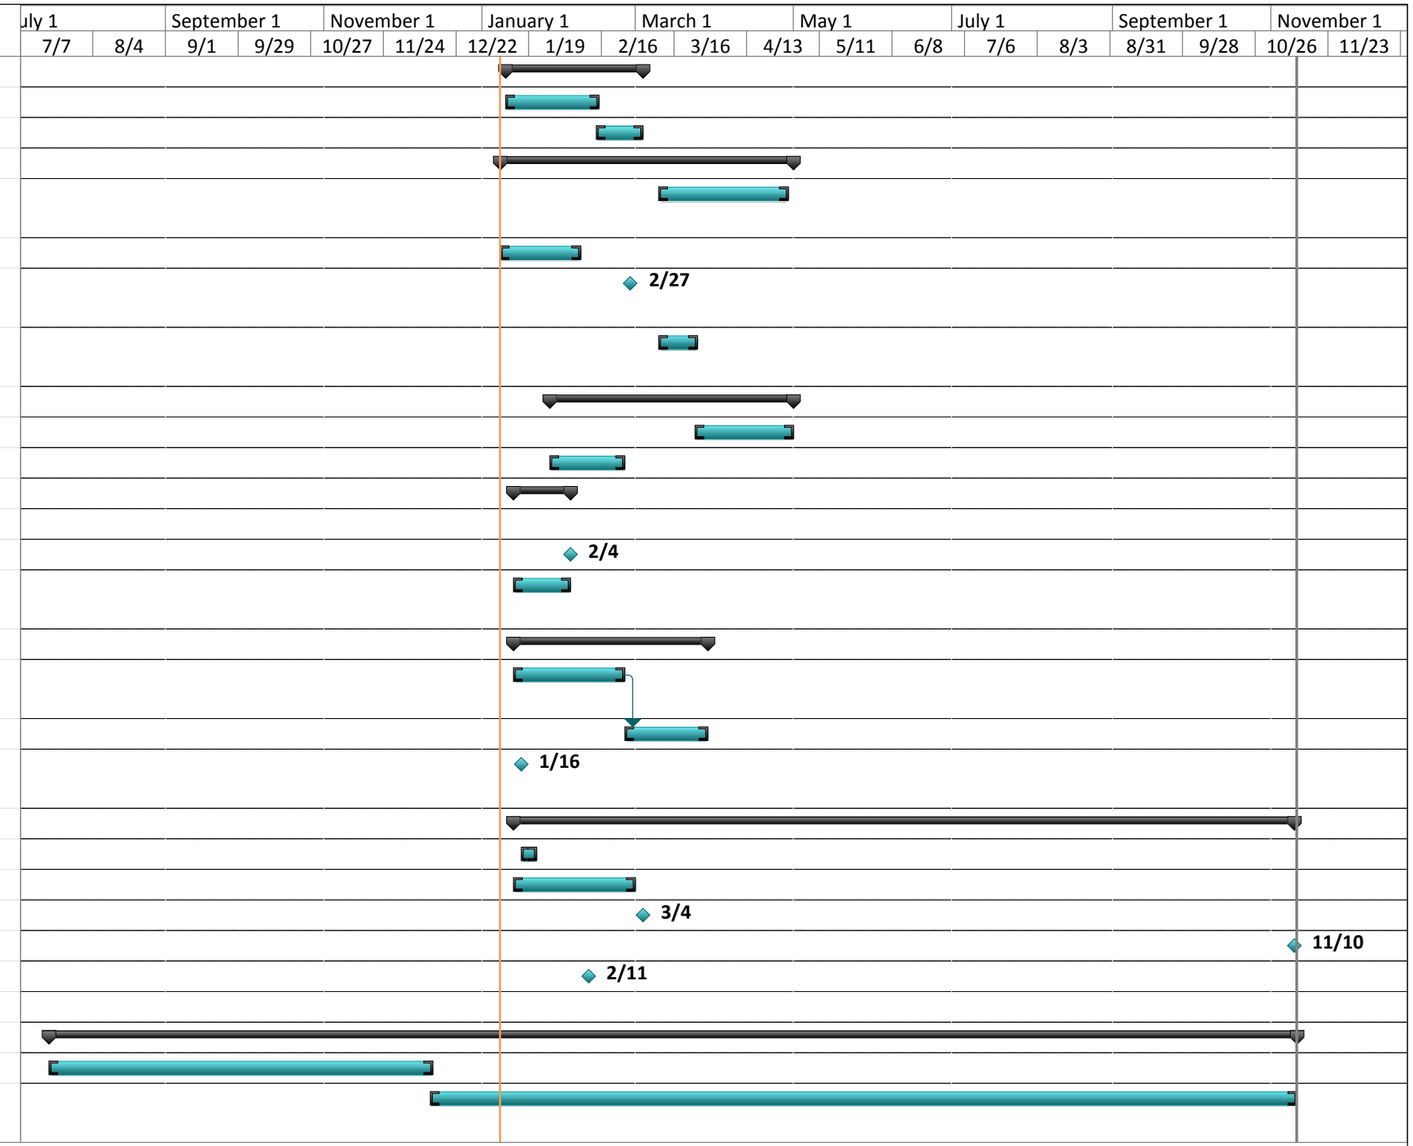

Project: BEDs_schedule_2012
Date: Wed 1/8/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
