05-5041 MARS HDD Project
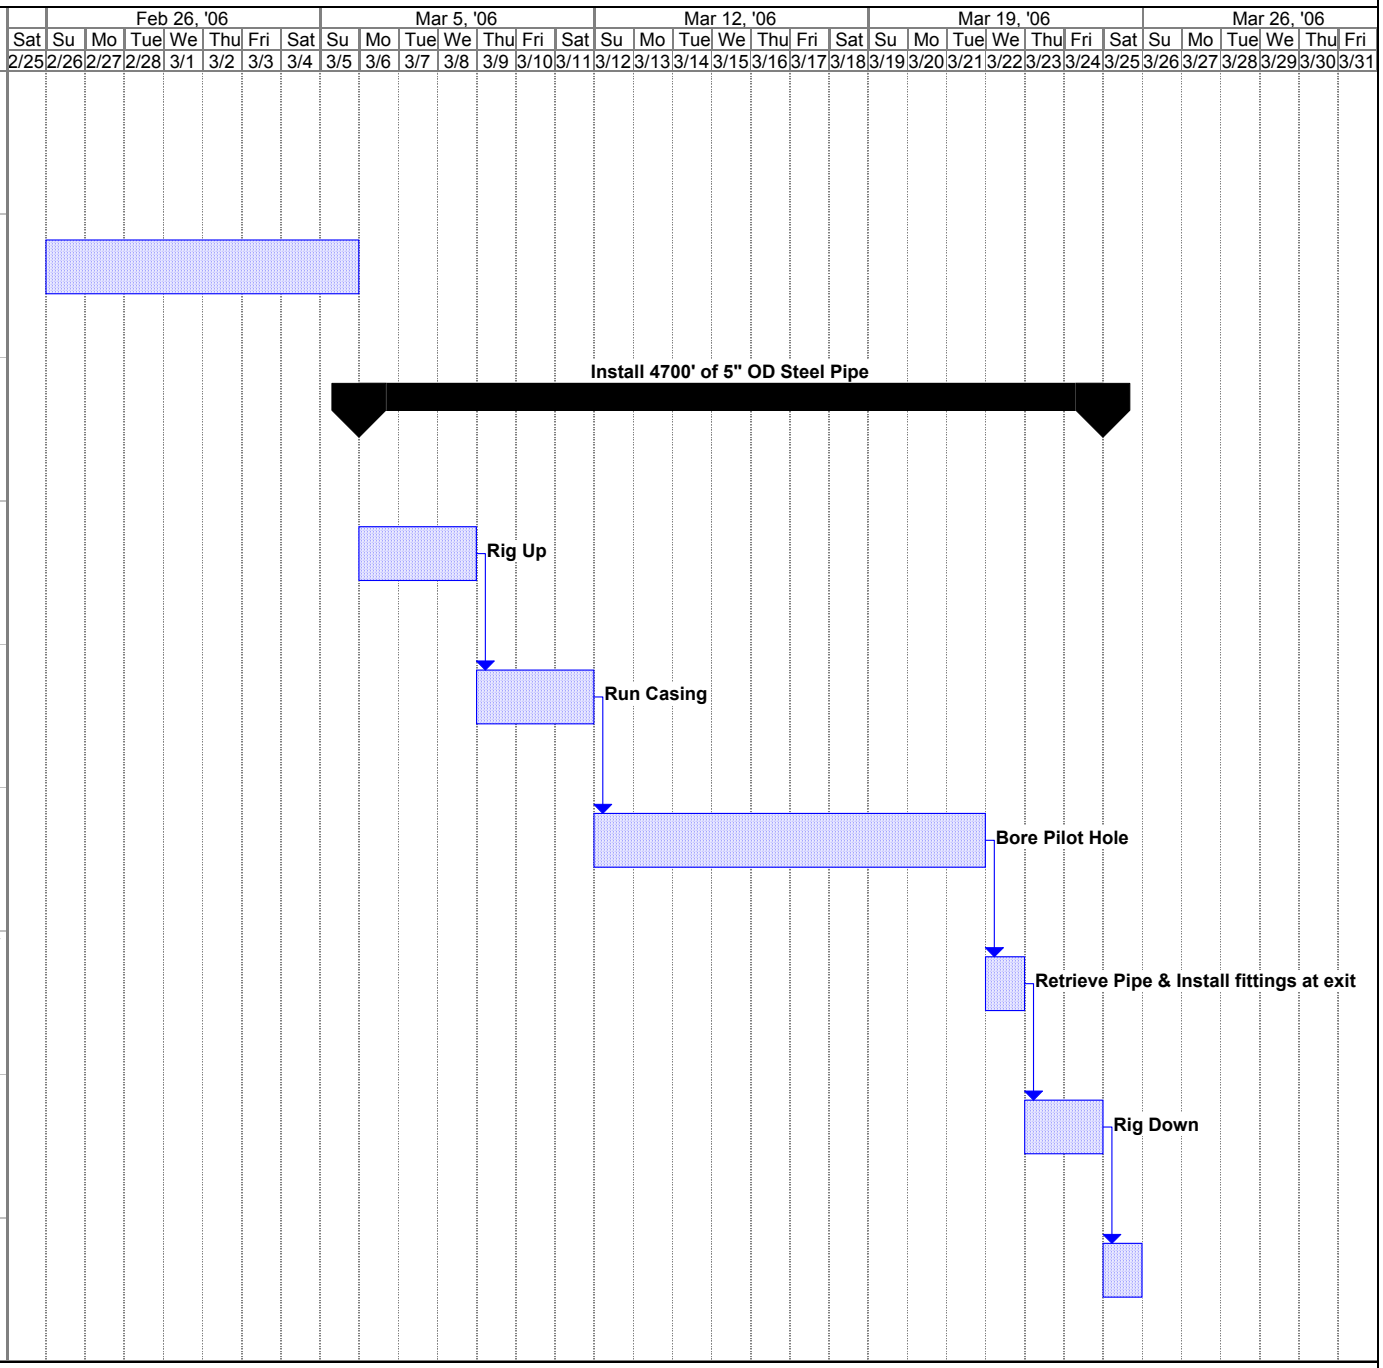
ID	Task Name	Duration
1		
2	Equipment starts arriving at MBARI	8 days
3	**Install 4700' of 5" OD Steel Pipe**	**19 days**
4	Rig Up	3 days
5	Run Casing	3 days
6	Bore Pilot Hole	10 days
7	Retrieve Pipe & Install fittings at exit	1 day
8	Rig Down	2 days
9	Mob Out	1 day?
