





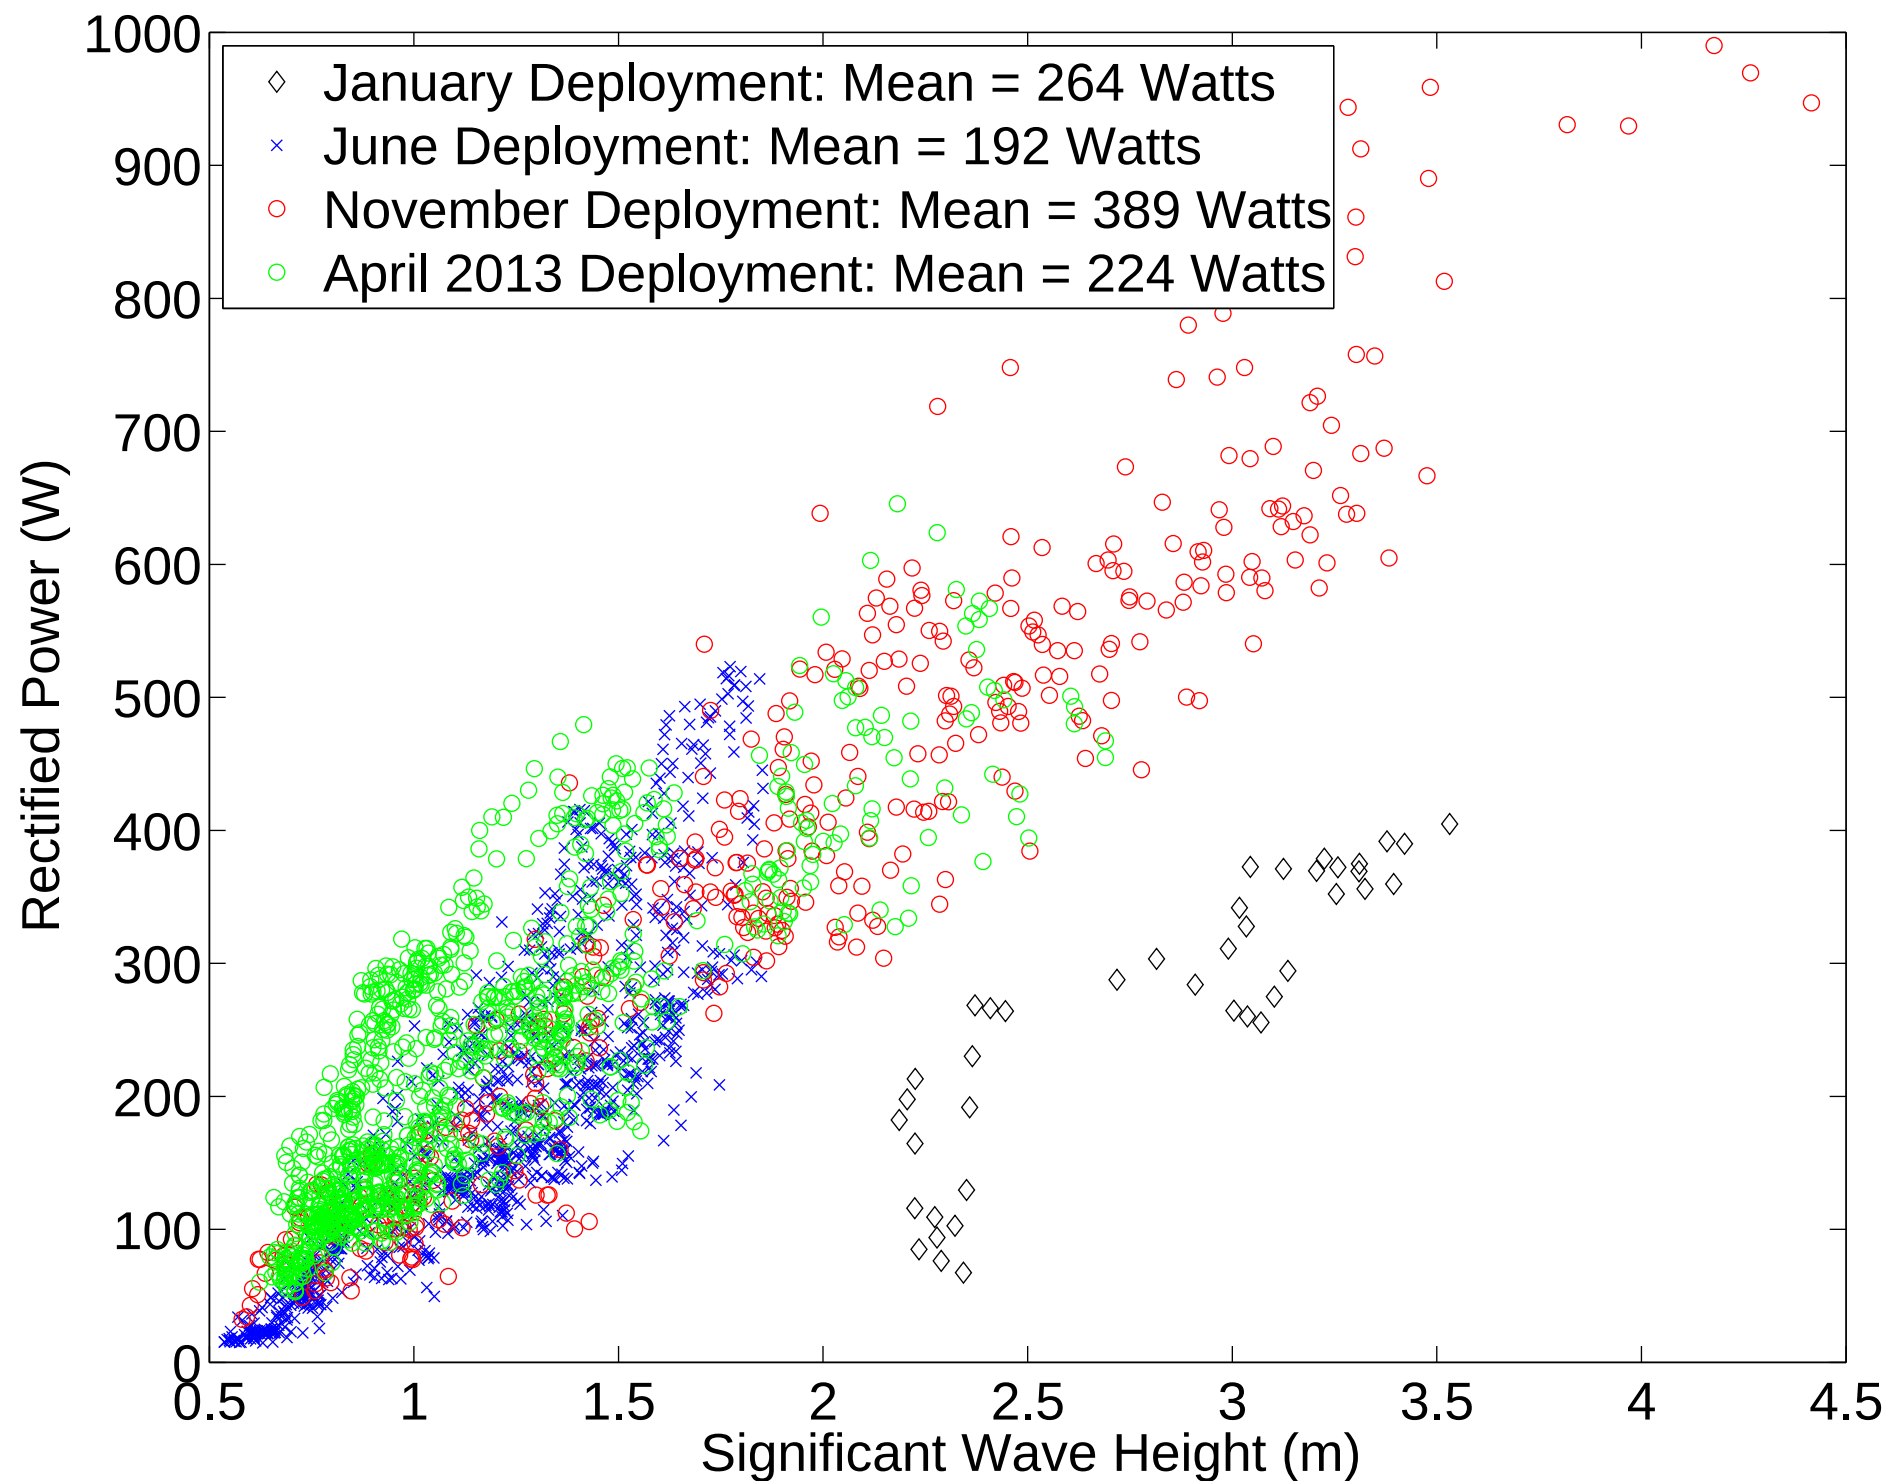

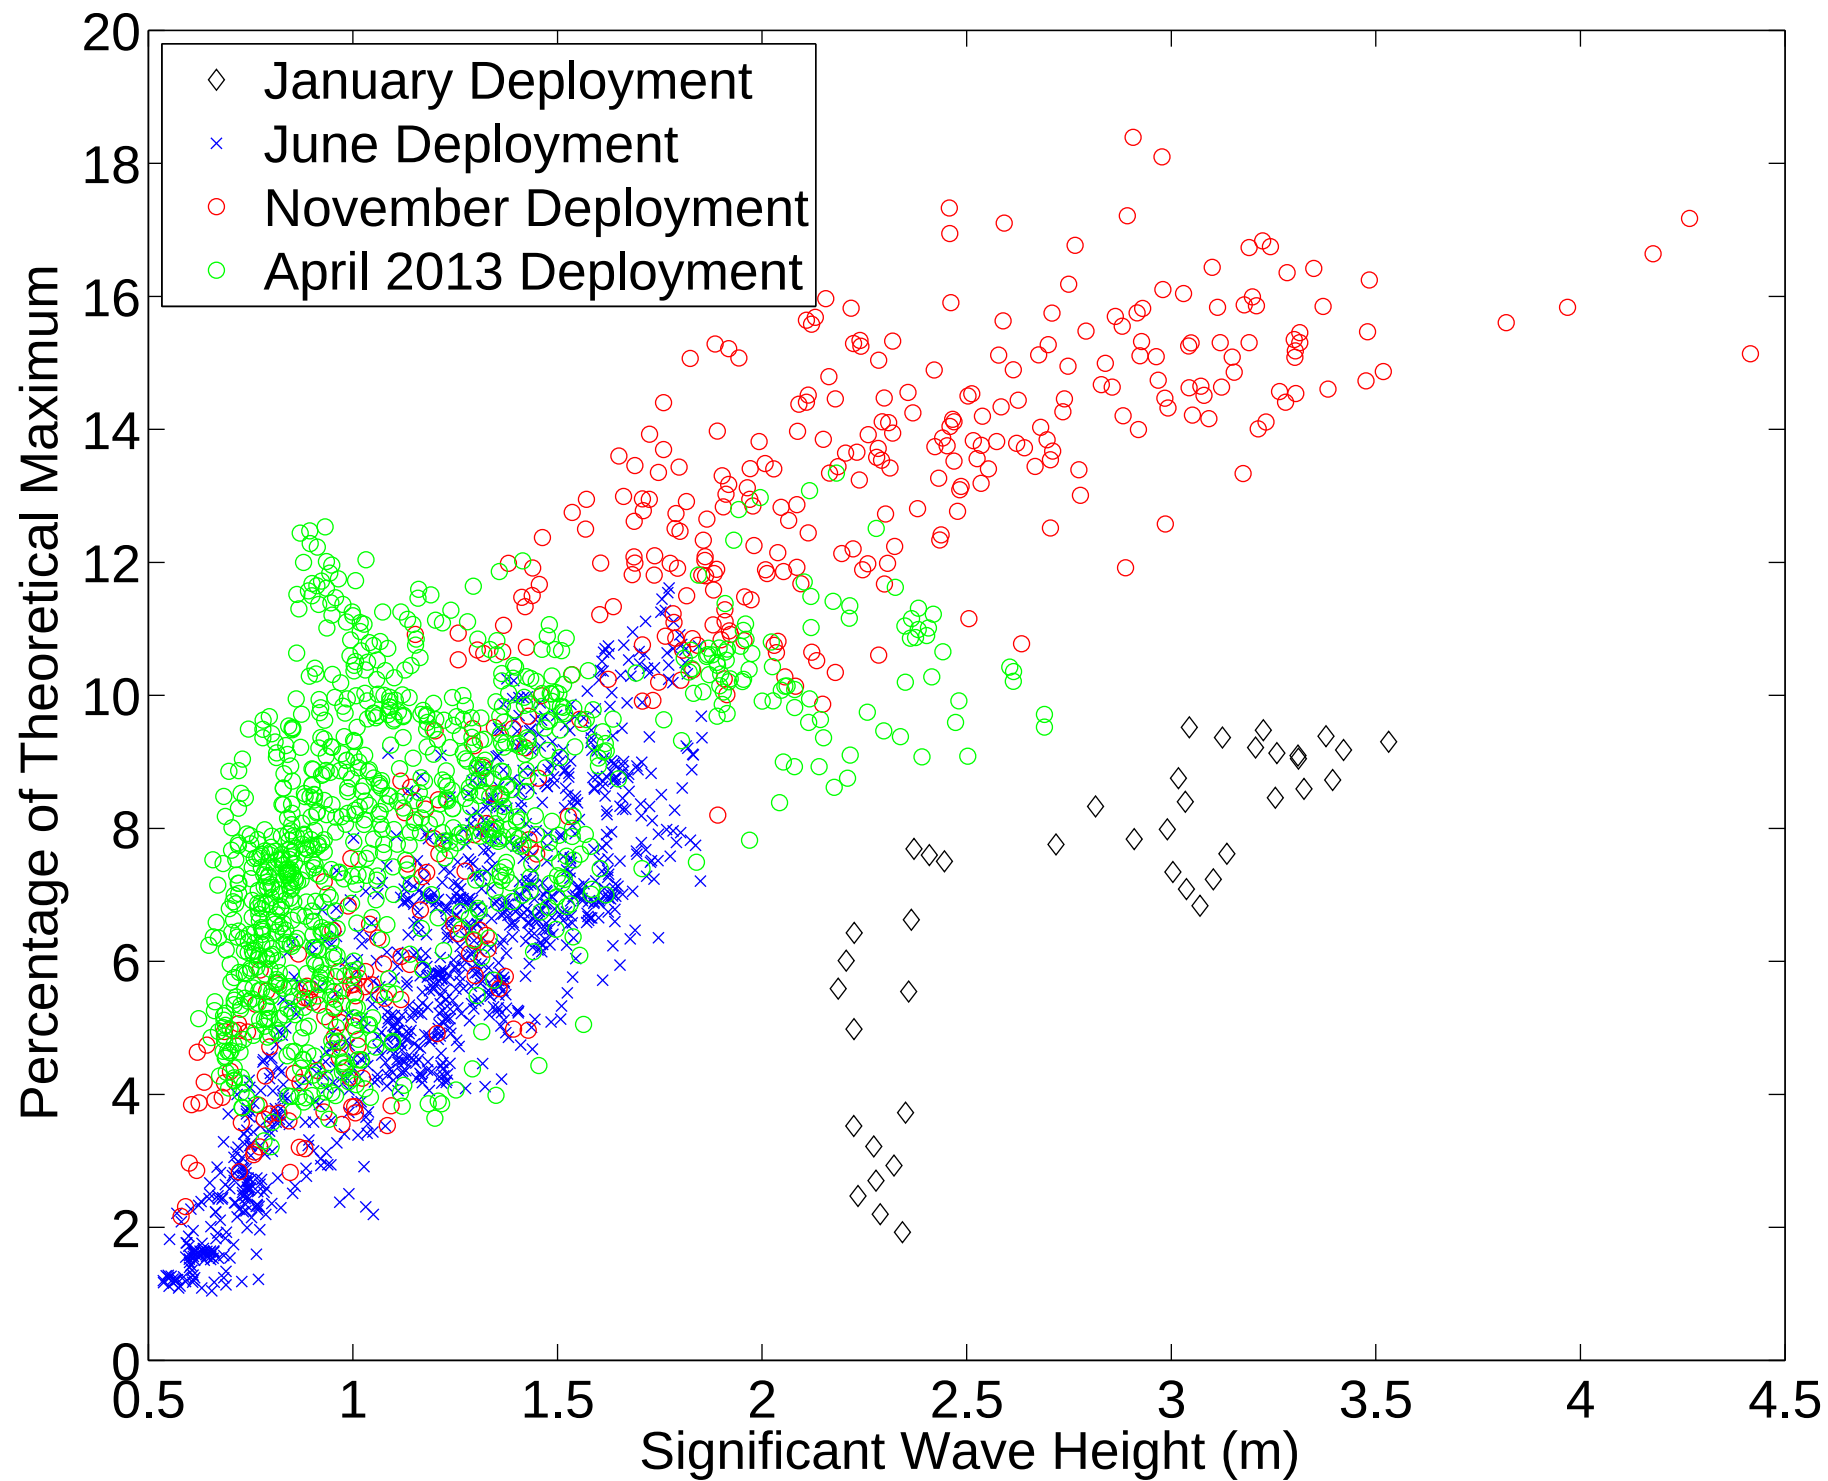


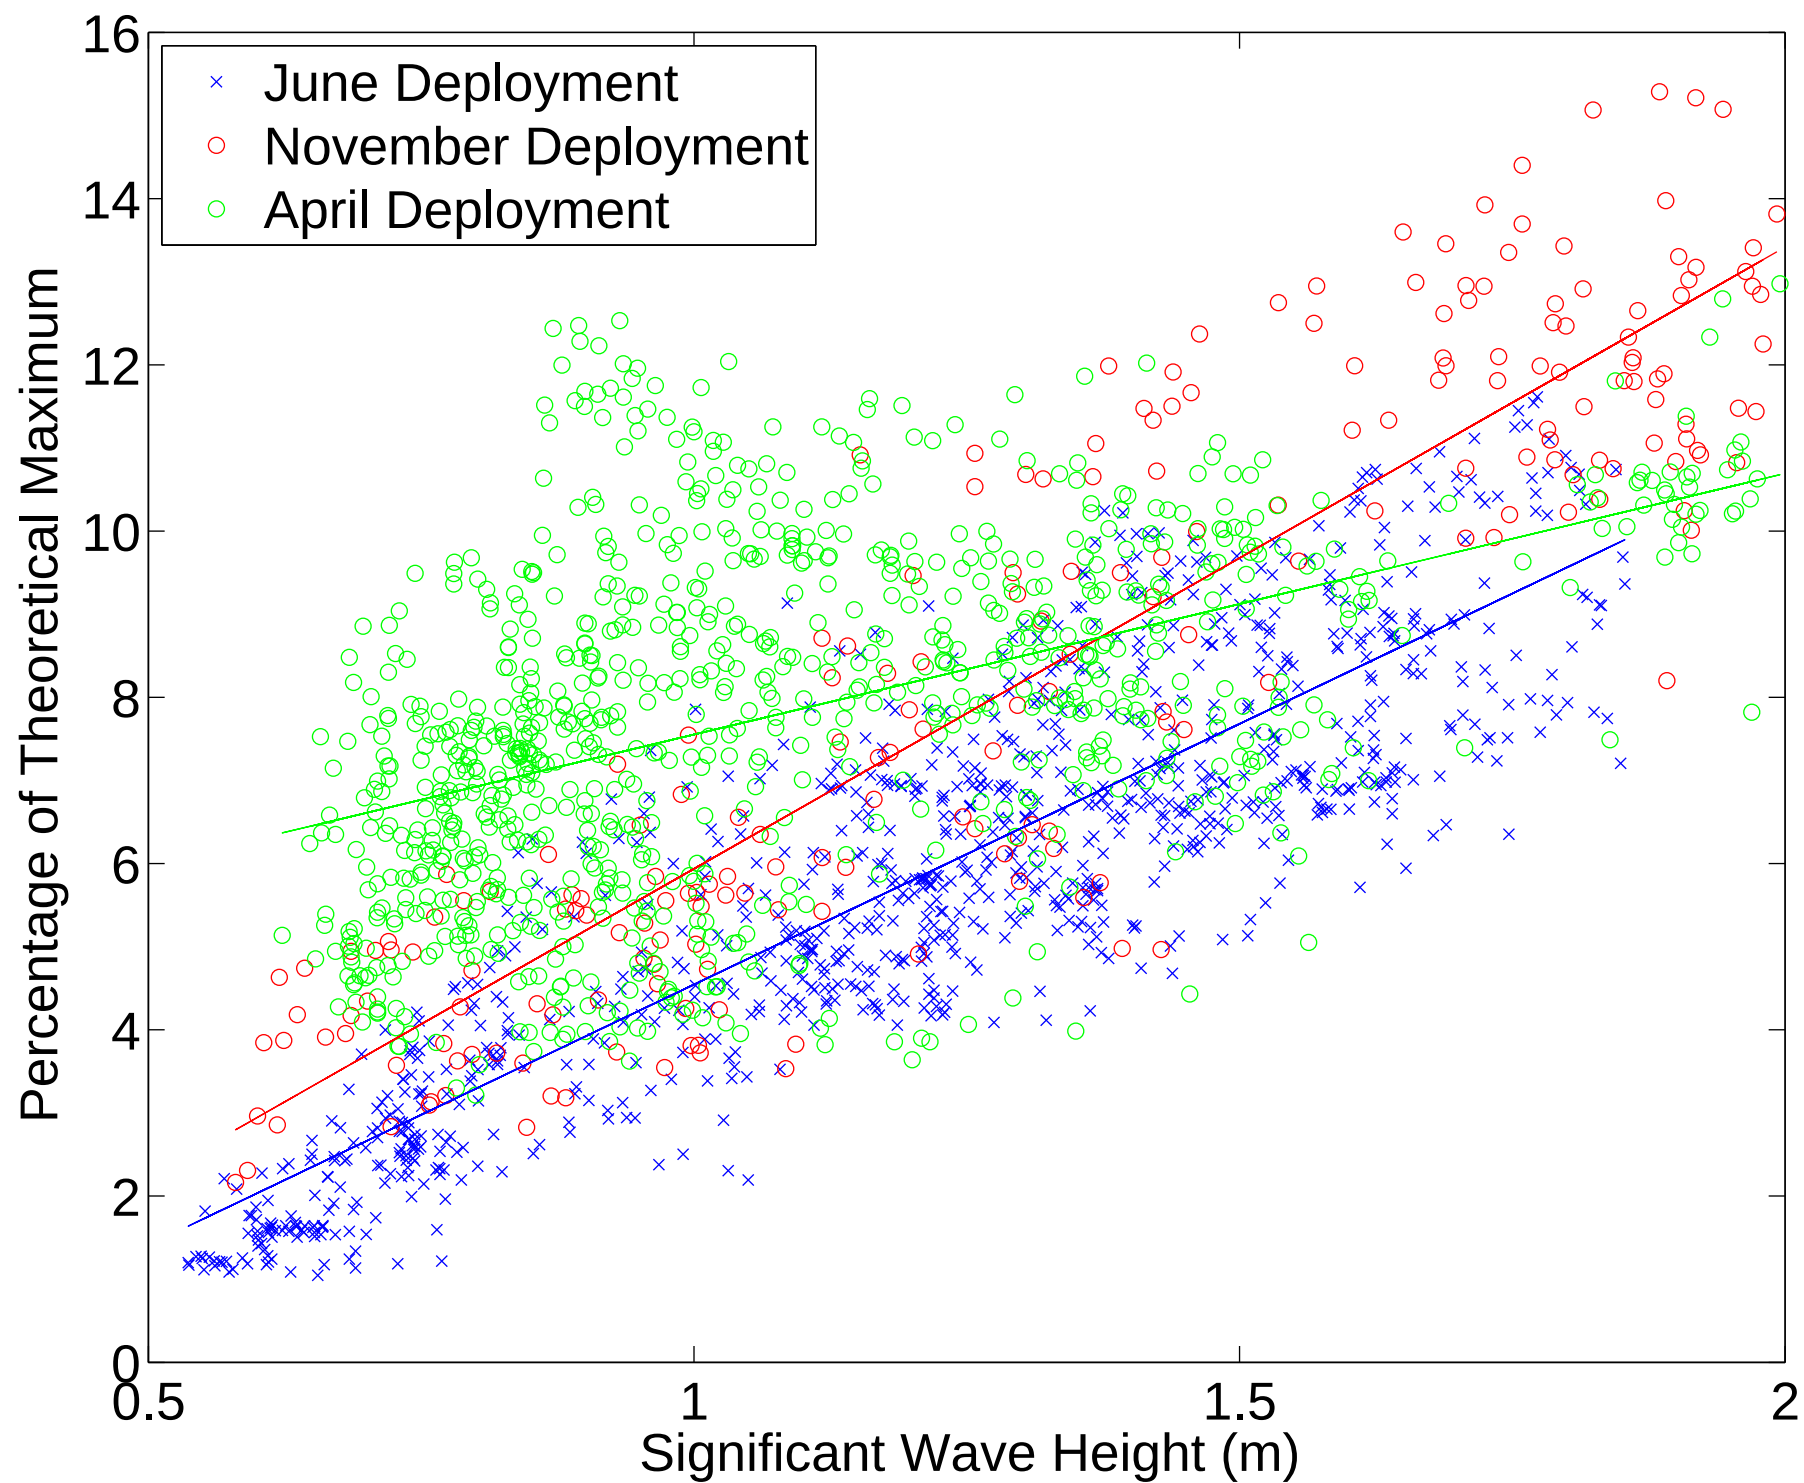

Monterey Bay May Conditions, Averaged from 2007–2012

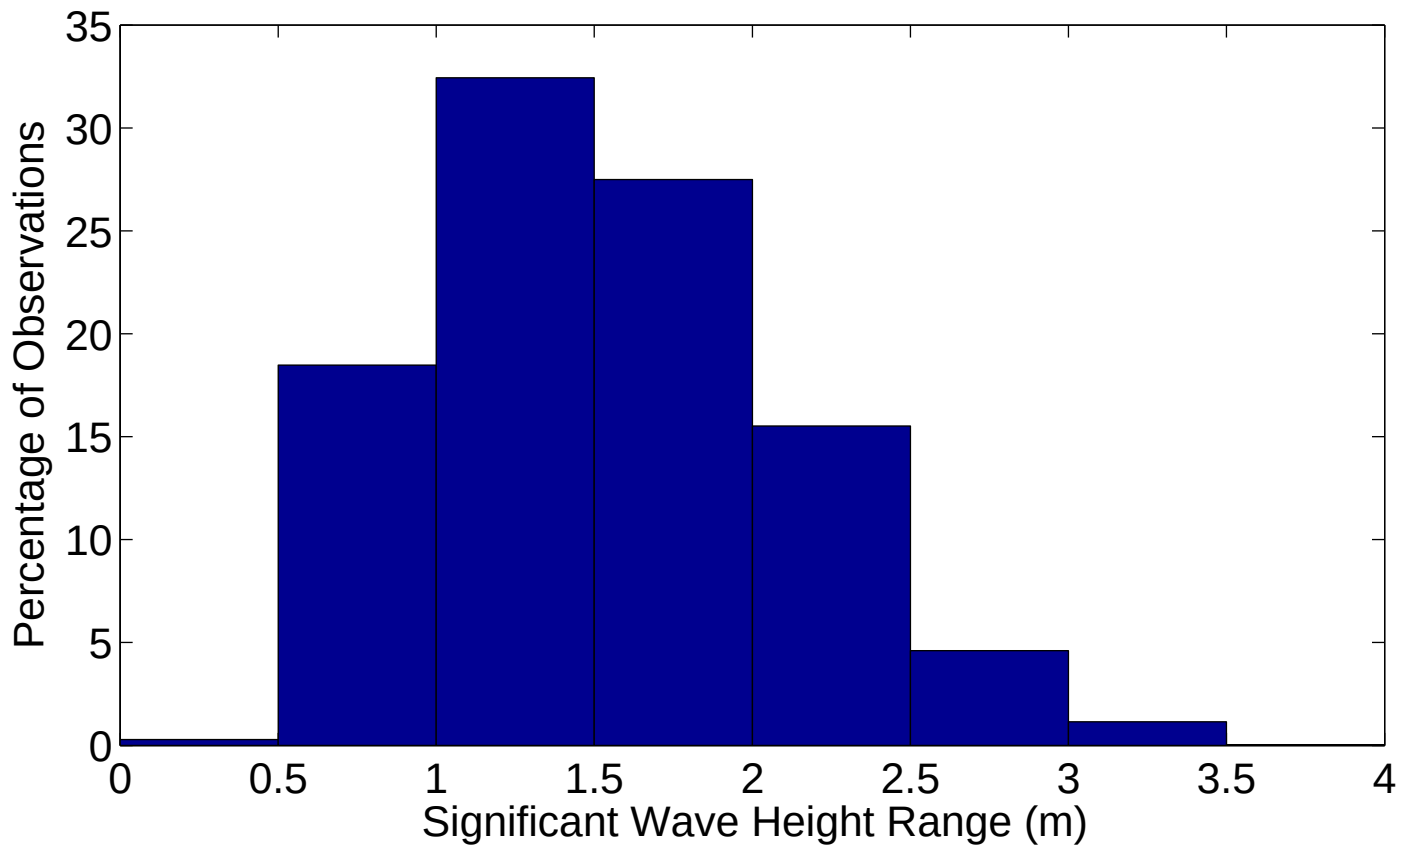



Conditions During Deployment (April 26 – May 10, 2013)

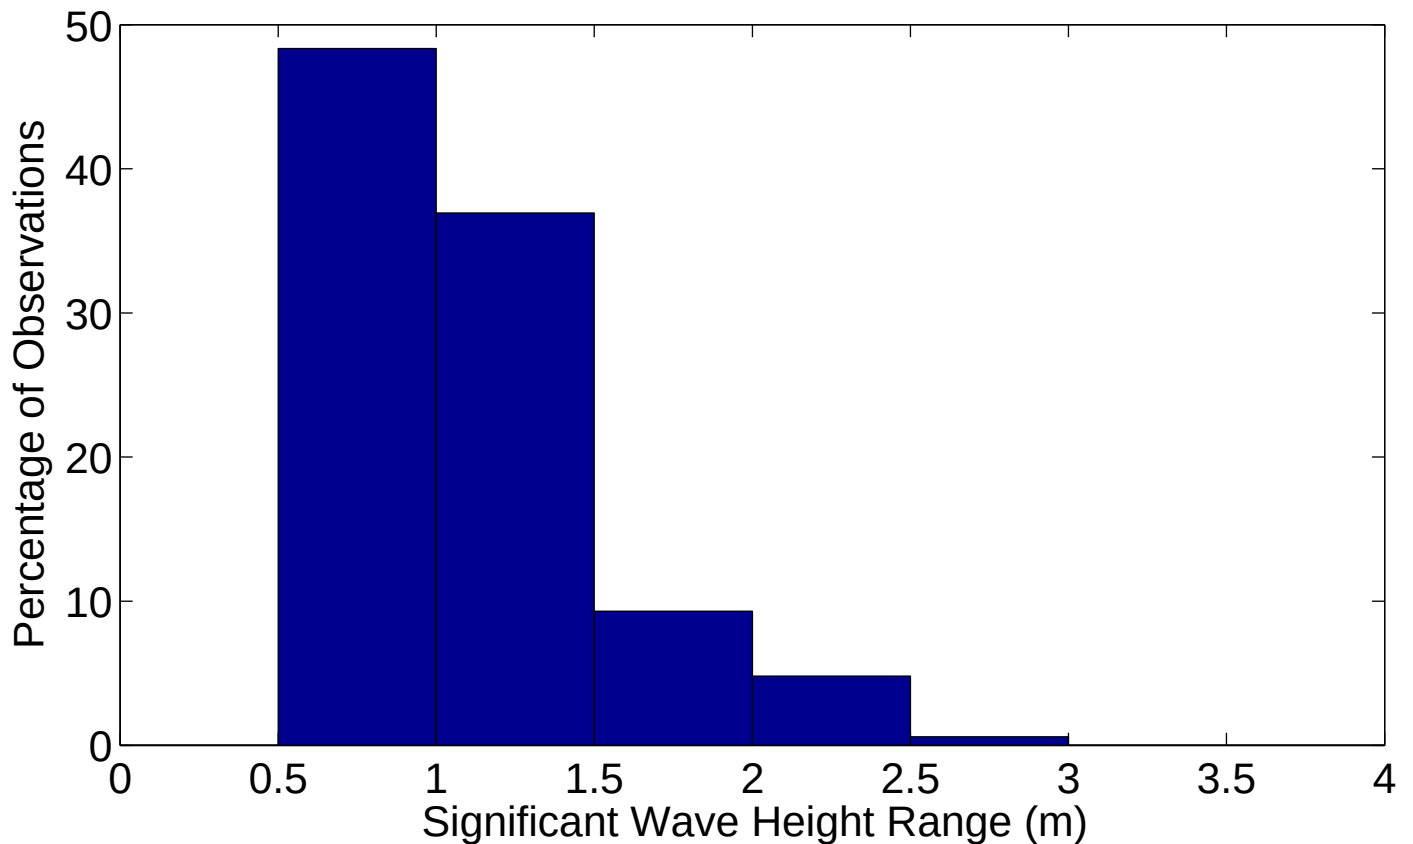

Financial Progress through May 9, 2013

The graph below shows the projects spend profile through May 9, 2013. The red line shows the original spending plan (from the original proposal), the green line shows the linear spend rate from the project inception to an end date that reflects a six month extension in the original period of performance. After September 2012 a second extension is represented by the change in slope of the green line. The blue line shows the actual spend rate.

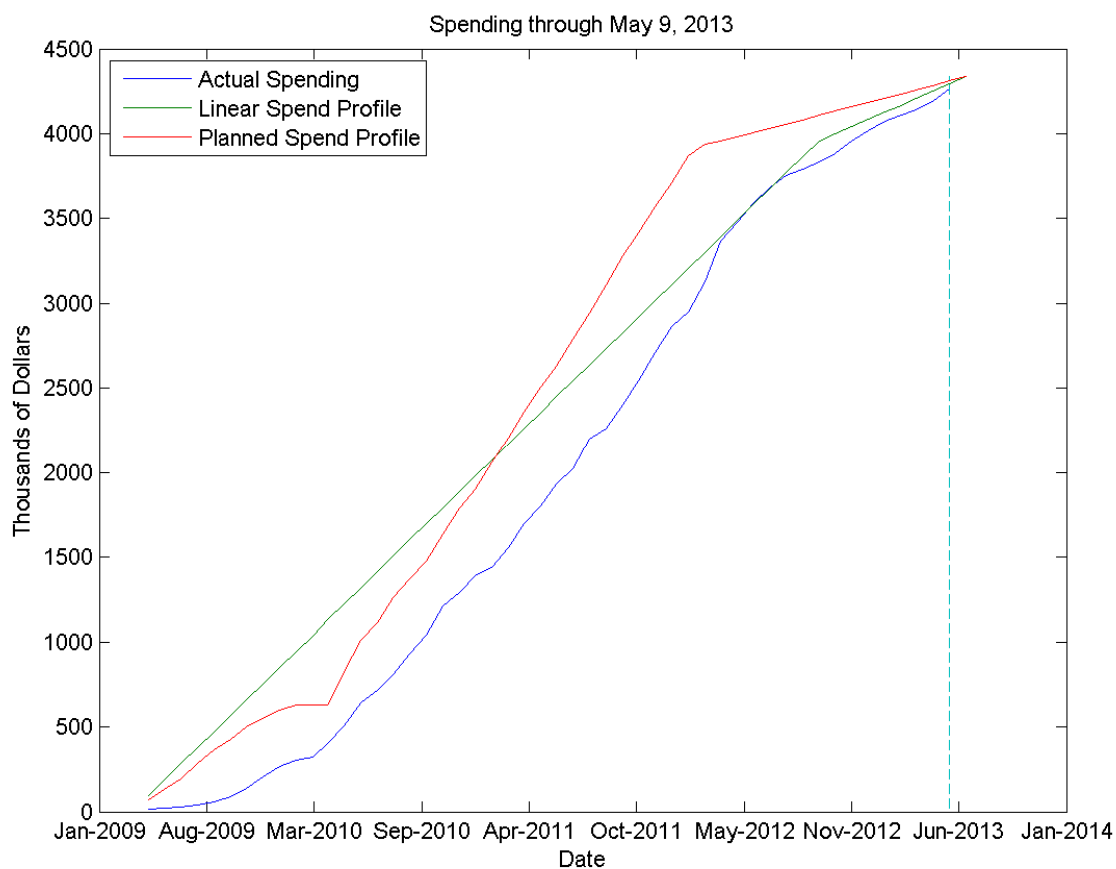

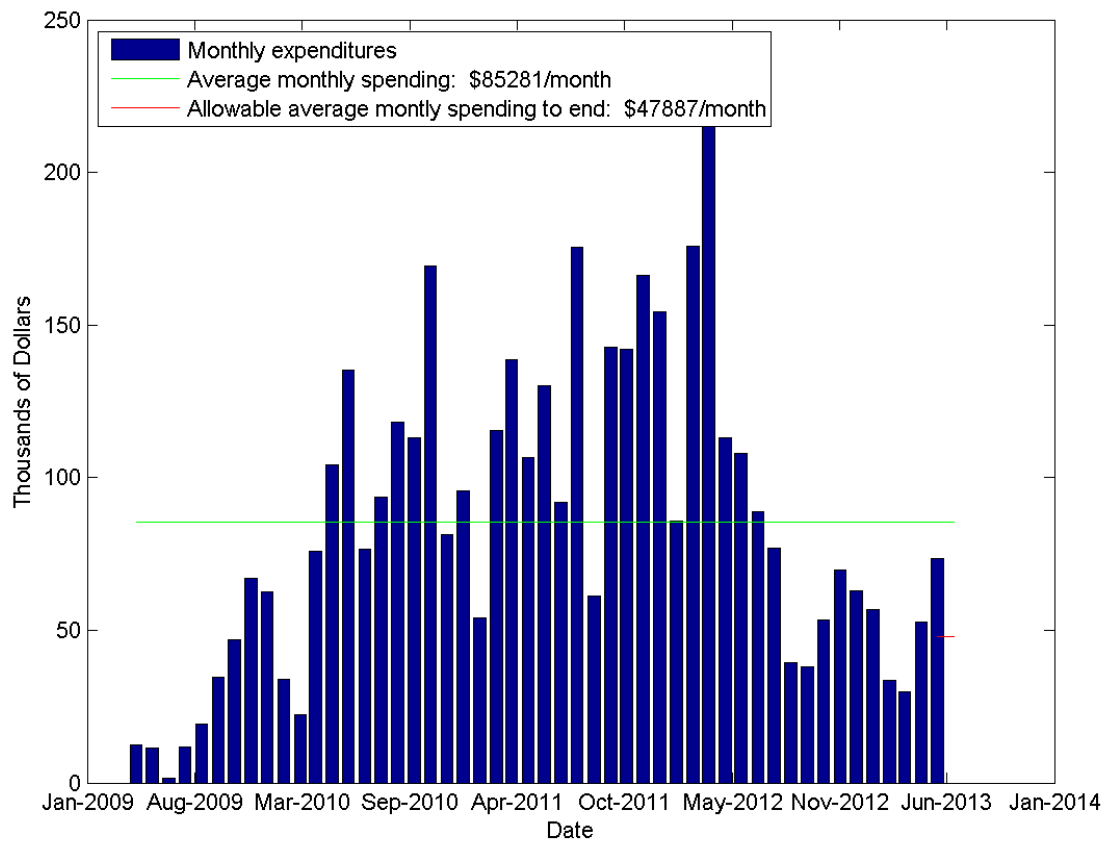

\$71831 Remains unspent

Updated: May 9, 2013

Report: May 01, 2016

Activity	Dates		Costs			Budget		Percent Complete/Spent (Est)			Spent	Remaining		
	Sub-tasks	Start	End	Labor (Days)	Material	Ship	(Burdened)		Labor (Days)	Material	Ship	(Burdened)	Dollars	Percentage
	2nd Test Deployment	4/26/2013	6/24/2013					\$17,640					\$15,190	86%
	System monitoring	4/26/2013	6/24/2013	4			\$4,898		50%			\$2,449		
	Inspection Trips	4/26/2013	6/24/2013	2			\$2,449							
	Recovery and Unload Boat	4/26/2013	6/24/2013	4		\$1,950	\$7,843		0%	0%		\$0		
	De-mobilization	4/26/2013	6/24/2013	2			\$2,449		0%			\$0		
	2nd Test Data Analysis	4/26/2013	6/24/2013					\$13,470					\$7,960	59%
	Correlation of test data and wave data	4/26/2013	6/24/2013	2			\$2,449		50%			\$1,225		
	Analysis of test data	4/26/2013	6/24/2013	7			\$8,572		50%			\$4,286		
	Test Report	4/26/2013	6/24/2013	2			\$2,449		0%			\$0		
	Final Project Report	4/26/2013	6/24/2013					\$34,288					\$24,002	70%
	Paper Preparation	4/26/2013	6/24/2013	14			\$17,144		30%			\$5,143		
	Final Data Analysis and Report Writing	4/26/2013	6/24/2013	14			\$17,144		30%			\$5,143		
	Homing Test	5/9/2013	6/24/2013					\$24,492					\$24,492	100%
	Test Setup	5/9/2013	6/24/2013	6			\$7,348		0%			\$0		
	Test at Sea	5/9/2013	6/24/2013	5			\$6,123		0%			\$0		
	Data Analysis	5/9/2013	6/24/2013	6			\$7,348		0%			\$0		
	Report	5/9/2013	6/24/2013	3			\$3,674		0%	0%		\$0		

Totals:

\$89,890

\$71,644
